

Hazel McCallion Campus Phase 2A Addition C Wing




Site Progress Photos as of September 27th,
2019



Thursday
September 27th,
2019

Photo taken
looking
Northeast
towards B-Wing.
Level 5
structural slab
has been
poured. Exterior
perimeter metal
stud progressing
to the fourth
Mezz. level.
While masonry
work has begun
within the
interior.

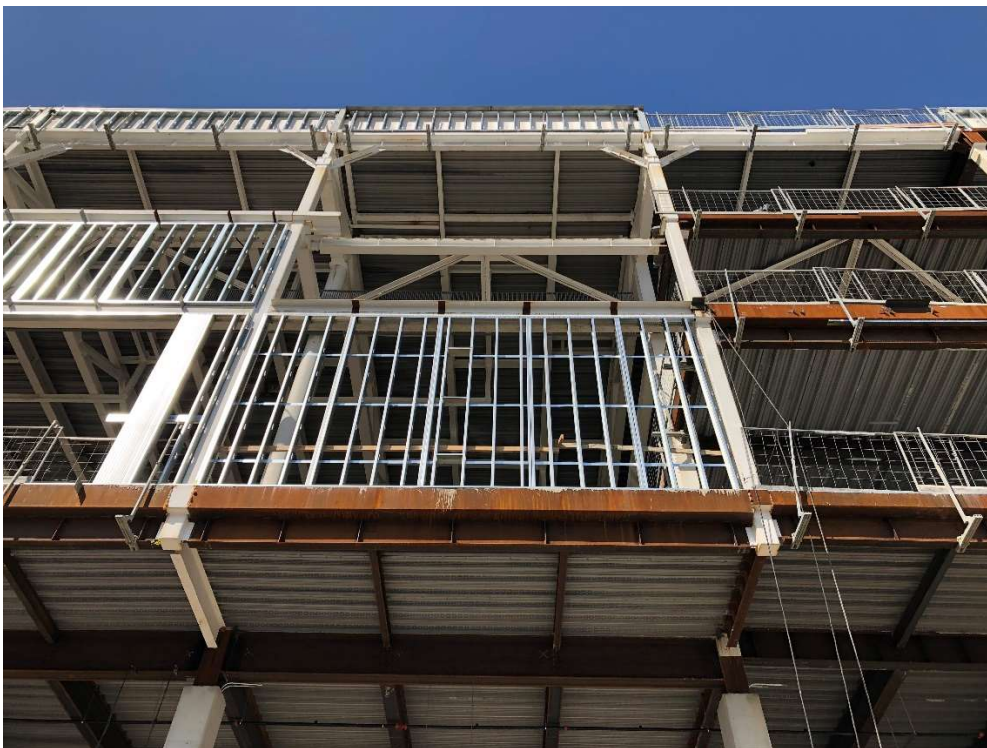



Thursday September 27th, 2019


Left Photo – Mechanical piping work continues within the B-Wing Penthouse, including draining the existing heating network for the interconnection to Phase 2a.

Right Photo – Installation of pumps along with associated piping within the B-Wing Penthouse Boiler room.



Thursday September 27th, 2019

Installation of electrical and AV under slab conduits continues at level 1, along with the installation of the AV under slab pathway for productions. Mechanical plumbing work within the ceiling space has begun within the kitchen C112b and washrooms C117/116.

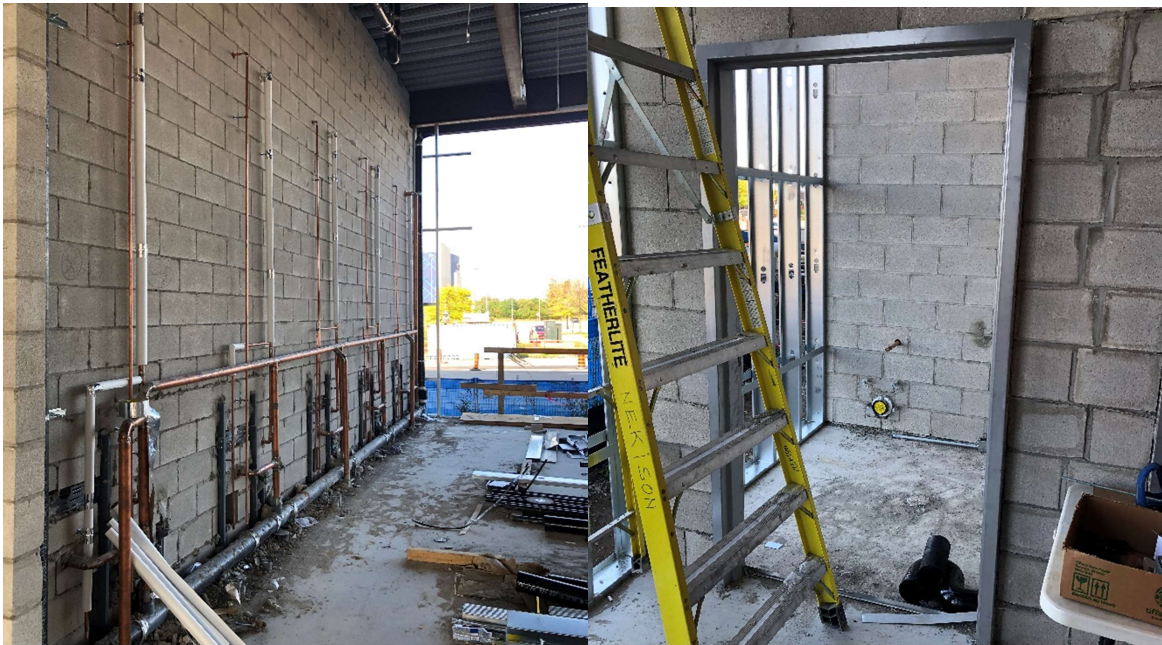



Thursday September 27th, 2019

Masonry interior partitions at Level 2 are completed along with with all associated mechanical plumbing and electrical rough-ins. Installation of ceiling mounted HVAC equipment has begun starting with fancoils and VAV boxes in C203 Common Lounge.





Thursday September 27th, 2019

Interior masonry partitions currently being installed on Level 3 along with all mechanical and electrical rough-ins. Perimeter metal studs currently being erected at the Northeast entrance. Curtain wall has begun installation along the north façade of the building starting with room C303 Lounge Games.

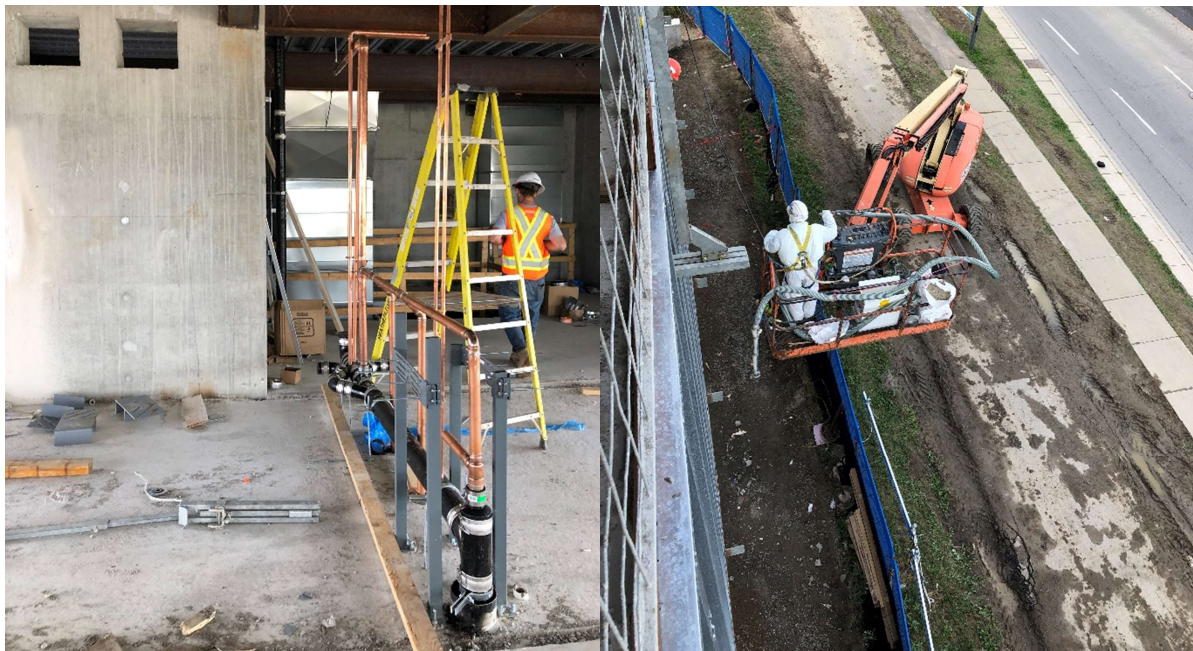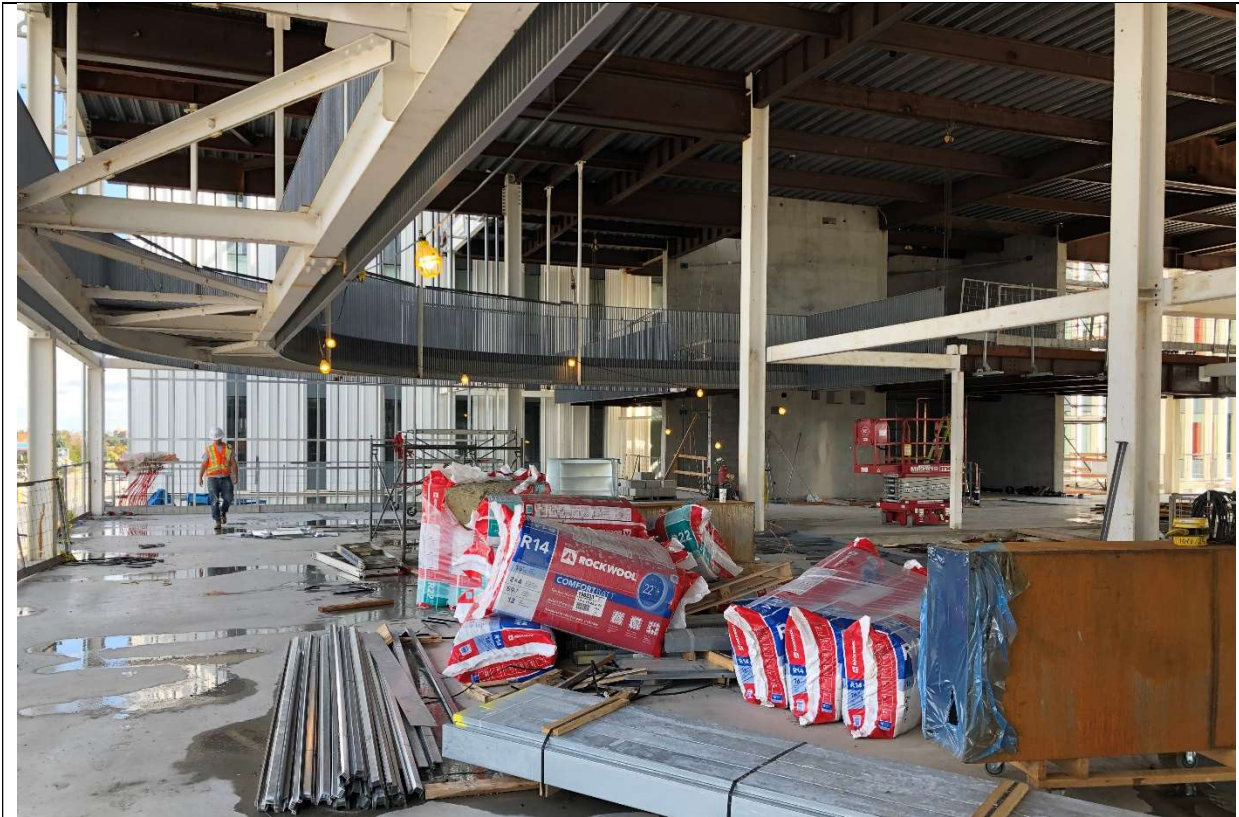

Thursday September 27th, 2019

Level 4 misc. metal guards installation nearing completion. Mechanical rough ins have begun within masonry partitions. Sprayed applied fire proofing is progressing along the north façade.

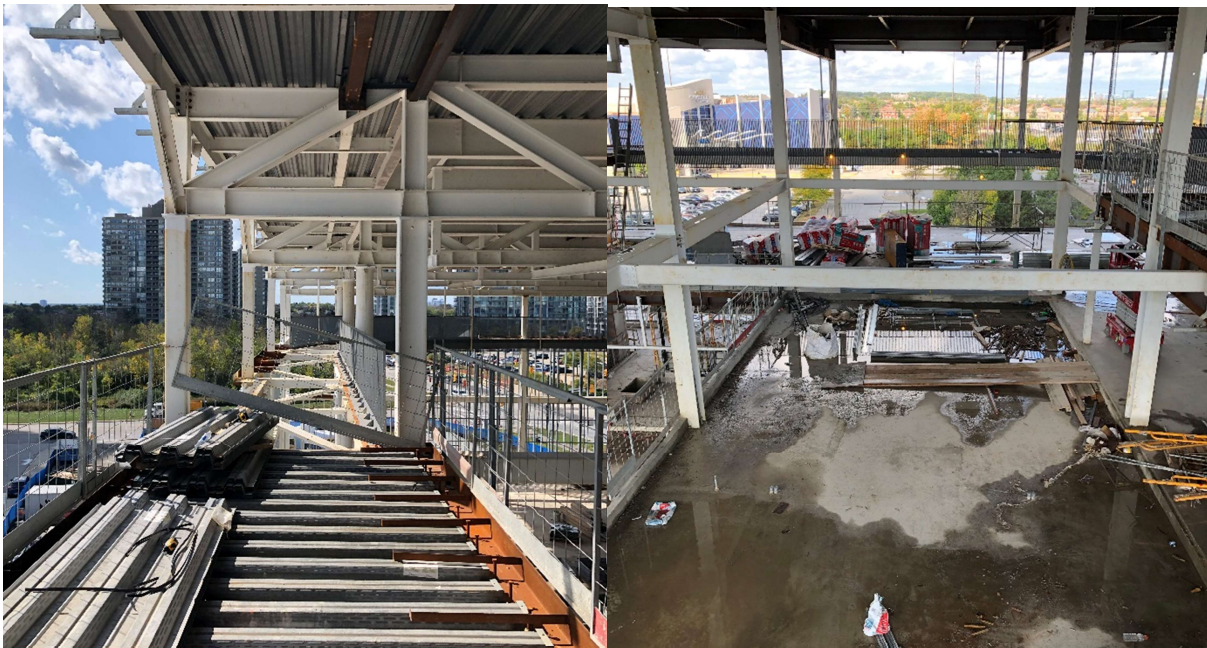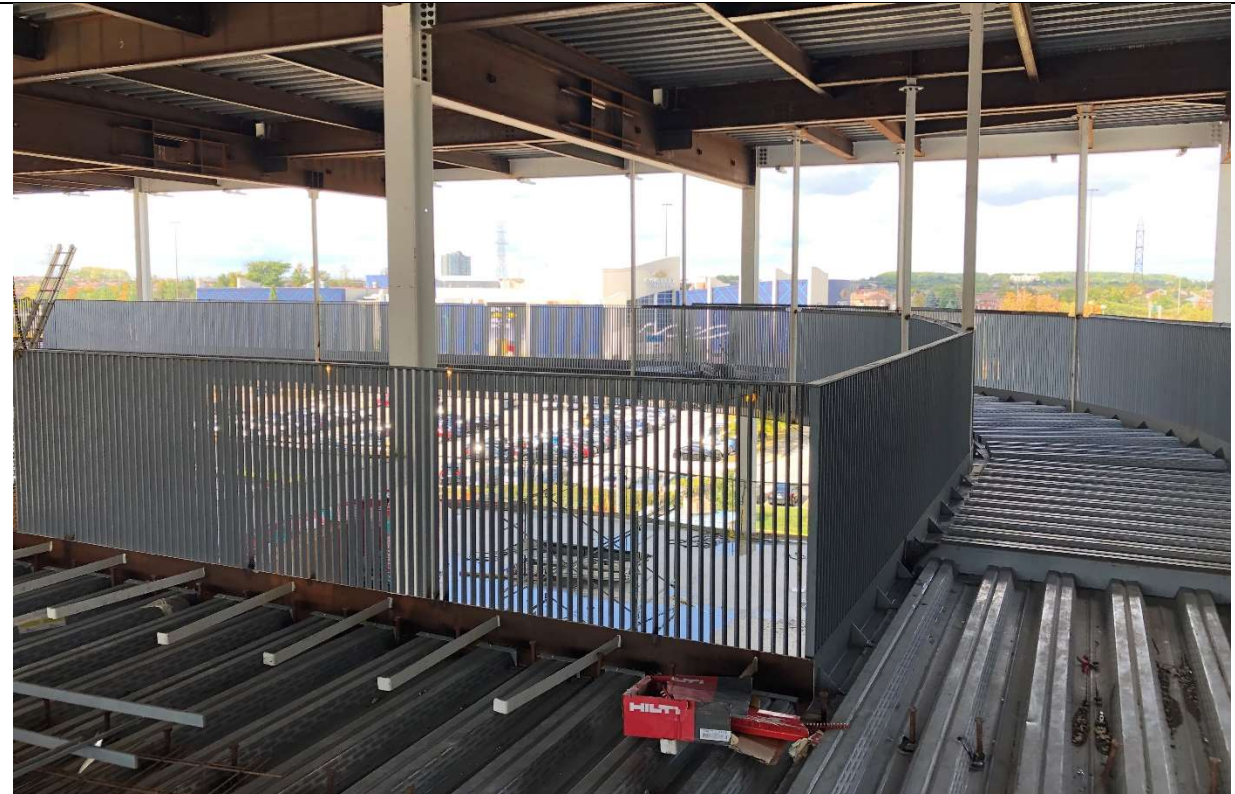


Thursday September 27th, 2019

Level 4 Mezzanine, track guard installation nearing completion, with metal decking flowing closely behind. Once decking has been completed the surface will be prepped for the structural concrete pour.



Thursday September 27th, 2019

Level 5 structural slab has been poured with mesh currently being laid, concrete topping to be poured Friday October 4th. Perimeter terraces have been boarded with GlasRoc.

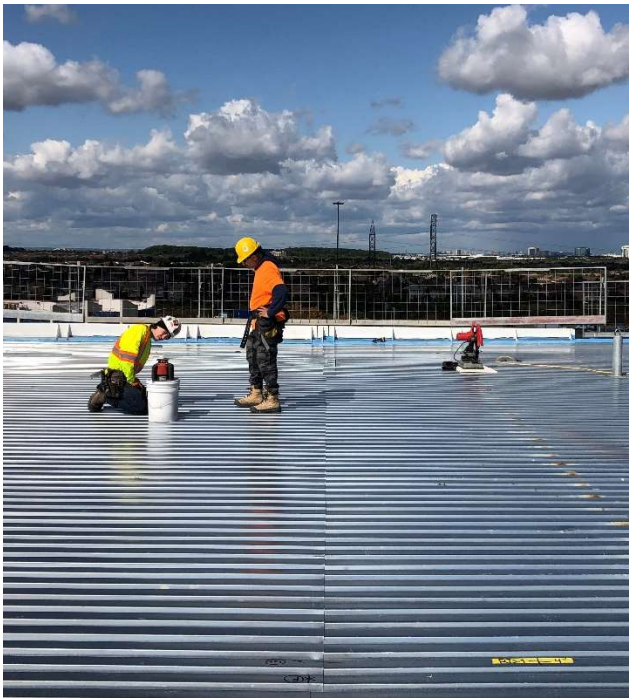

Thursday September 27th, 2019

Roof Level – work continues at the perimeter parapet wall and deck sleeving, roofing starting with Dens Deck and vapour barrier to begin shortly.
